


**Marine Working Group – Marine Works Update, February 2021**


**Marine Work Update – Western Expansion Area**

Marine work completed in the West since the January 18, 2021 update is as follows:

1. Completed Rip Rap placement for slope protection at Centerm’s Western expansion.
2. Prepared the two newly installed Caissons for precast installation at Centerm Berth 6.
3. Work on Sheet pile wall adjacent to Centerm Berth 6.

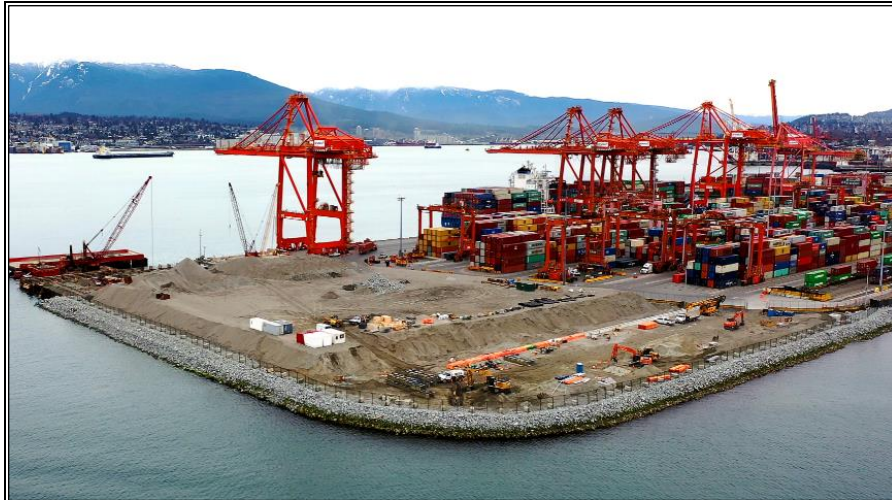

*Rip Rap placement*

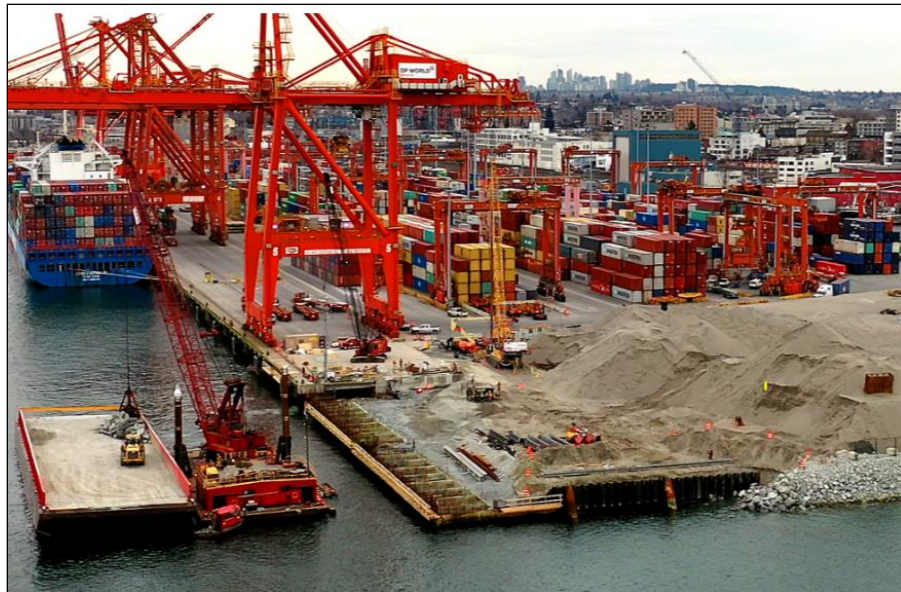


*Sheet pile wall and area of precast panel installation*

### Marine Work Update – East Expansion Area

Marine work completed in the East since the January 18, 2021 update:

1. Completed Rip Rap placement for slope protection at Centerm’s Eastern expansion

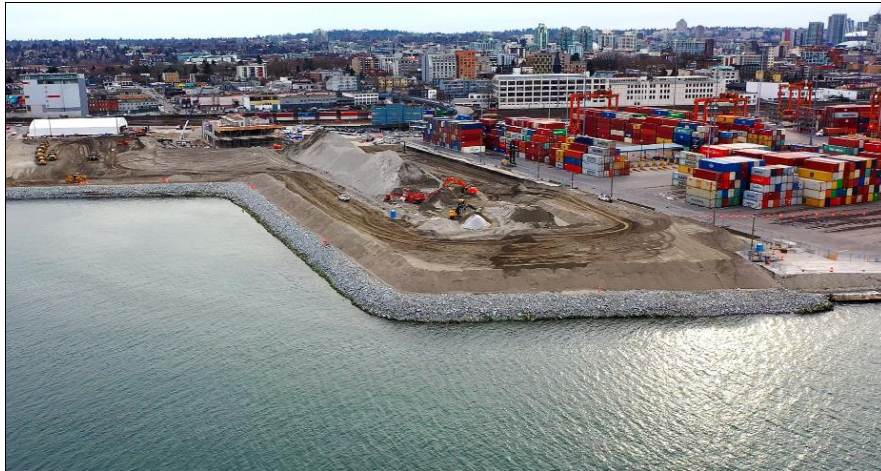


*Eastern expansion, East of Centerm Berth 2*

### Marine Work Outlook & Work Hours and Days

The following marine work will be undertaken over the next few weeks:

1. Demobilization activities in the East expansion area (February/March)
2. Installation of precast panels on the West (End of Feb/early March)
3. Temporary demobilization of CXP’s marine rig (March)
4. Intermittent works around Berth 6 (March)

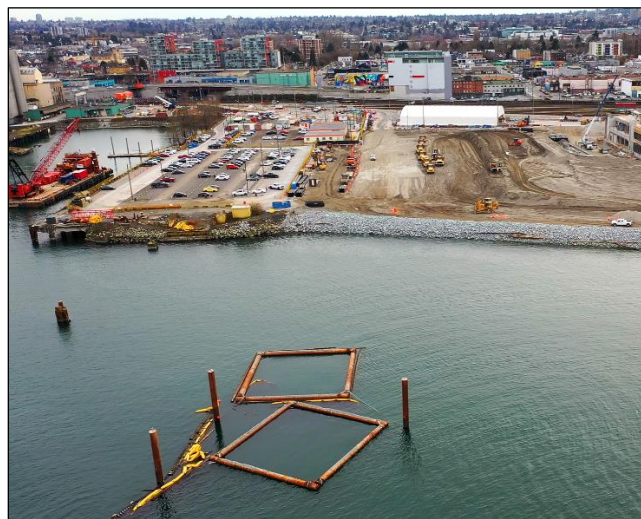

*Silt curtains and temporary mooring piles to be demobilized*

#### Work Hours and Days:

- Full time marine work has completed. All future marine work will be in a support capacity, conducted intermittently as needed, Monday to Saturday, 08:00 to 20:00.

### Vessels on Site in March 2021

Vessels on site in March 2021 will be as follows:

1. Barge-mounted crawler crane (1 unit on East/West Expansion work areas as needed).
  - Demobilizing in early March, only returning intermittently as required by the Project for marine craning support.
  - Anticipate the Barge-mounted crawler crane back approximately May/June 2021 for sand preload removal activities for approximately 1 month.
2. Support tug - Seaspam "JRW"
3. Survey vessel "Fraser Surveyor"
4. Dive vessel as needed.

### Notifications

- Navigational Warning in place for intermittent works (NW-P-0273-21) - expires Mar. 17, 2021. Will be renewed as needed to support CXP's ongoing intermittent marine works and, the removal of preload sand / placement of dyke toe protection in the Western expansion area in the June timeframe.
- NOTAM (I052521) in place for CXP's intermittent marine work.
- Advance notifications of marine works impacting stakeholders will be issued as needed.

### Contacts for Stakeholder Feedback, Concerns, Questions

CXP is available to discuss and address any concerns and/or operational impacts caused by our intermittent marine work which will be ongoing to June 2021. If you have any questions, concerns, or would like more information regarding this Marine Work Update, please contact:

**Zoë Strand, CXP Communications Manager; 604-910-5785 | [Zstrand@CXP-JV.com](mailto:Zstrand@CXP-JV.com)**

**Sherry Kennedy, CXP Marine Construction Manager; 604-813-5679 | [Skennedy@CXP-JV.com](mailto:Skennedy@CXP-JV.com)**

### Timing of Next Marine Update

CXP's next marine work update is planned for the week of March 22, 2021.
